

**GOVERNMENT OF PUDUCHERRY**  
**PROJECT INFORMATION SHEET**

**Name of the Department : Electricity Department, Puducherry .**

Sl. No		
1.	Date of furnishing information / Updation	<b>15-10-2019</b>
2.	Name of the Project / Survey / Study	<b>R-APDRP (PART-B)</b>
3.	Objectives :	
	(a)	<b>ACHIEVEMENT OF AT&amp;C LOSSES TO 15%</b>
	(b)	<b>IMPROVEMENT IN QUALITY AND RELIABILITY OF POWER SUPPLY IN URBAN AREA</b>
	(c)	<b>CUSTOMER SATISFACTION</b>
	Project Status :	<b>ON GOING</b>
5.	Project Cost ( Rs. in Crores ):	<b>Rs. 84.78 CRORES</b>
	(a) International e.g. World Bank , JICA, EU, etc.	<b>NIL</b>
	(b) Government of India	<b>Rs. 21.195 CR FROM GOVT OF INDIA BY AVAILING LOAN FROM PFC</b>
	(c) Government of Puducherry	<b>NIL</b>
	(d) Loan (PFC.)	<b>Rs 63.585 Cr. AS COUNTERPART FUND BY AVAILING LOAN FROM PFC</b>
	(e) Others	
	Total ( a + b + c + d + e )	<b>Rs 84.78 CRORES</b>
6.	<b>Project Timeline :</b>	
	<b>Date of Sanction by MOP, GOI</b>	<b>8/3/2013</b>
	<b>Date of Sanction by GOP</b>	<b>27-12-2013</b>
	<b>Date of Commencement</b>	<b>8/3/2013</b>
	<b>Date of Completion</b>	<b>December 2019</b>
7.	Implementing Agency	<b>ELECTRICITY DEPT, PUDUCHERRY</b>
	<b>PROJECT STATUS</b>	
8.	<b>Works awarded</b>	<b>Rs. 60.172 crores</b>
9	<b>Amount received from PFC under GOI Loan</b>	<b>Rs. 12.717 crores (Rs.10.65 Cr. on 28.03.2014 / Rs. 2.06 Cr. On 08.05.2014)</b>
10	<b>Amount received from PFC under counter-part fund</b>	<b>: Rs. 39.250 crores ( Rs. 16.5 on 31.03.2017/ Rs. 6.61 cr. on 31.03.2018/ Rs.10.30 cr on 12-03-2019 / Rs. 05.84 cr. on 27-09-2019)</b>
11	<b>Total amount received</b>	<b>: Rs. 51.967 crores</b>
12	<b>Amount Spent / incurred for various works</b>	<b>: Rs. 46.127 crores</b>

**GOVERNMENT OF PUDUCHERRY, ELECTRICITY DEPARTMENT.**



**As on 15-10-2019**[illegible]

[illegible]





[illegible]

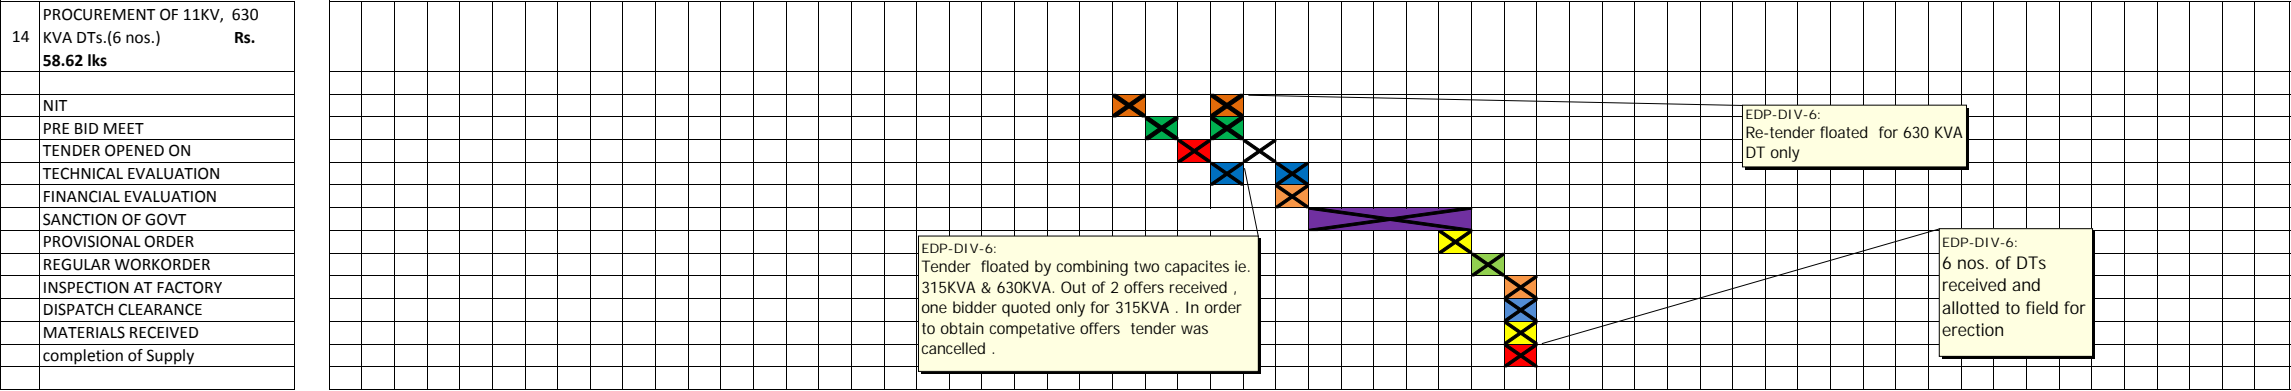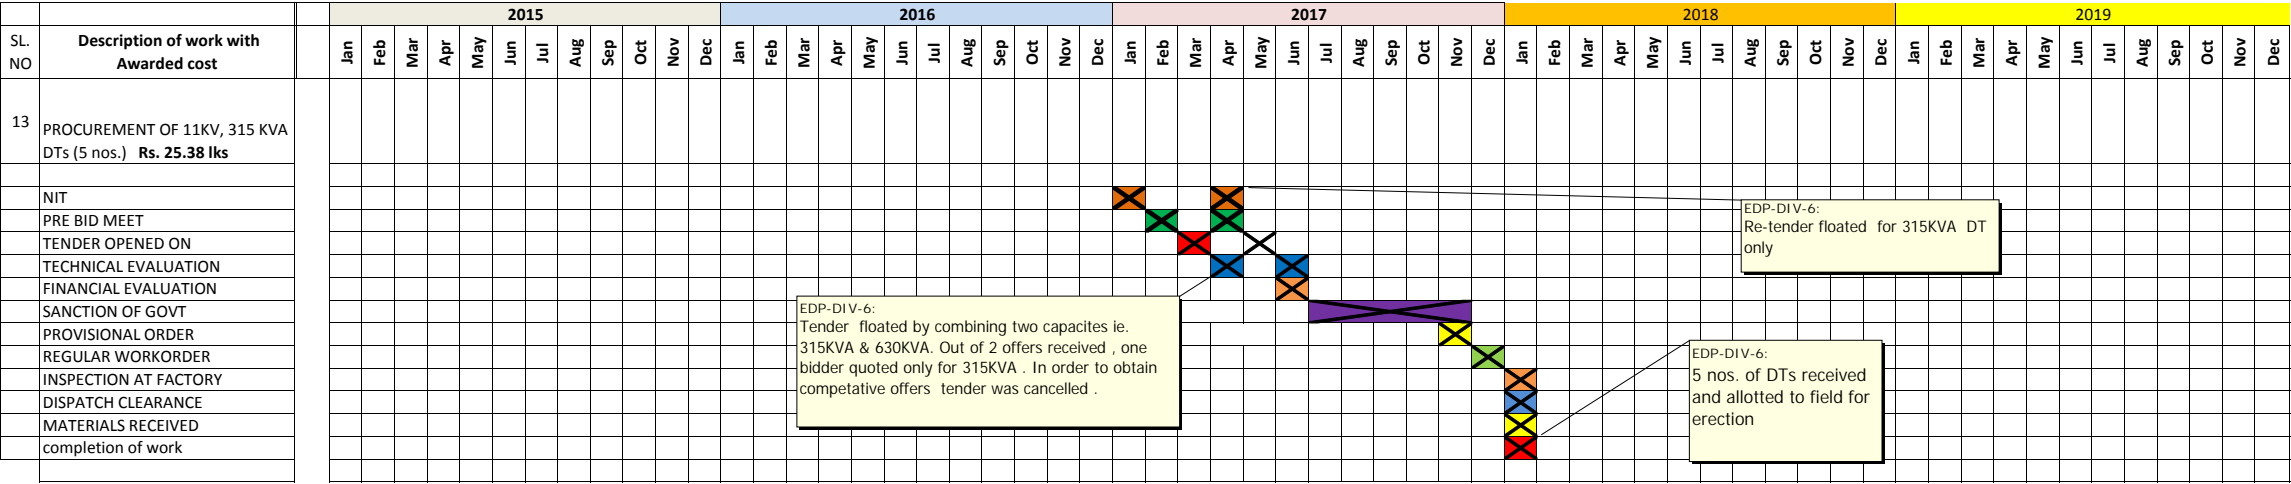







		2015												2016												2017												2018												2019											
SL. NO	Description of work with Awarded cost	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec												
19	Provision of 22KV Sectionalizers / Load Break switches. <b>Rs. 867.00lks</b>																																																												
	NIT																																																												
	PRE BID MEET																																																												
	TENDER OPENING																																																												
	TECHNICAL EVALUATION																																																												
	FINANCIAL EVALUATION																																																												
	SANCTION OF THE GOVT																																																												
	PROVISIONAL ORDER																																																												
	REGULAR WORKORDER																																																												
	DISPATCH CLEARANCE																																																												
	MATERIALS RECEIPT																																																												
	ERECTION OF SECTIONALIZERS completion of work																																																												

EDP-DIV-6:  
Tender cancelled as L1 bidder could not produce proof for despatching sample units to ITALY for conduct of Type Tests.

20	<b>PROVISION OF APFC PANELS Rs. 416.56 lks</b>																																																		
	REGULAR WORKORDER																																																		
	PRE BID MEET																																																		
	TENDER OPENING																																																		
	TECHNICAL EVALUATION																																																		
	FINANCIAL EVALUATION																																																		
	SANCTION OF THE GOVT																																																		
	PROVISIONAL ORDER																																																		
	REGULAR WORKORDER																																																		
	DISPATCH CLEARANCE																																																		
	MATERIALS RECEIPT																																																		
	ERECTION OF APFC PANELS completion of work																																																		

EDP-DIV-6:  
First tender floated in 2014 was cancelled, since the amount quoted by the L1 bidder is 100% higher than the tendered amt. Re- Tender floated was cancelled due to modification in tech. specification.

EDP-DIV-6:  
Only one offer received. Due to insufficient bids, the tender was cancelled.

EDP-DIV-6:  
Tender cancelled since none of the bidders were qualified

EDP-DIV-6:  
Financial bid under evaluation

