

GOVERNMENT OF PUDUCHERRY
PROJECT INFORMATION SHEET

Name of the Department : Electricity Department, Puducherry .


Sl. No		
1.	Date of furnishing information / Updation	30-08-2018
2.	Name of the Project / Survey / Study	R-APDRP (PART-B)
3.	Objectives :	
	(a)	ACHIEVEMENT OF AT&C LOSSES TO 15%
	(b)	IMPROVEMENT IN QUALITY AND RELIABILITY OF POWER SUPPLY IN URBAN AREA
	(c)	CUSTOMER SATISFACTION
	Project Status :	ON GOING
5.	Project Cost (Rs. in Crores):	Rs. 84.78 CRORES
	(a) International e.g. World Bank , JICA, EU, etc.	NIL
	(b) Government of India	Rs. 21.195 CR FROM GOVT OF INDIA BY AVAILING LOAN FROM PFC
	(c) Government of Puducherry	NIL
	(d) Loan (PFC.)	Rs 63.585 Cr. AS COUNTERPART FUND BY AVAILING LOAN FROM PFC
	(e) Others	
	Total (a + b + c + d + e)	Rs 84.78 CRORES
6.	Project Timeline :	
	Date of Sanction by MOP, GOI	8/3/2013
	Date of Sanction by GOP	27-12-2013
	Date of Commencement	8/3/2013
	Date of Completion	March 2019
7.	Implementing Agency	ELECTRICITY DEPT, PUDUCHERRY
8.	PROJECT STATUS	
	Works awarded	Rs. 43.883 crores
9	Amount received from PFC under GOI Loan	Rs. 12.717 crores (Rs.10.65 Cr. on 28.03.2014 / Rs. 2.06 Cr. On 08.05.2014)
10	Amount received from PFC under counter-part fund	Rs. 23.11 crores (Rs. 16.5 on 31.03.2017/ Rs. 6.61 cr. on 31.03.2018)
11	Total amount received	Rs. 35.827 crores
12	Amount Spent / incurred for various works	Rs. 32.383 crores


GOVERNMENT OF PUDUCHERRY, ELECTRICITY DEPARTMENT.

R-APDRP (PART-B) STATUS REPORT

[illegible]

[illegible]

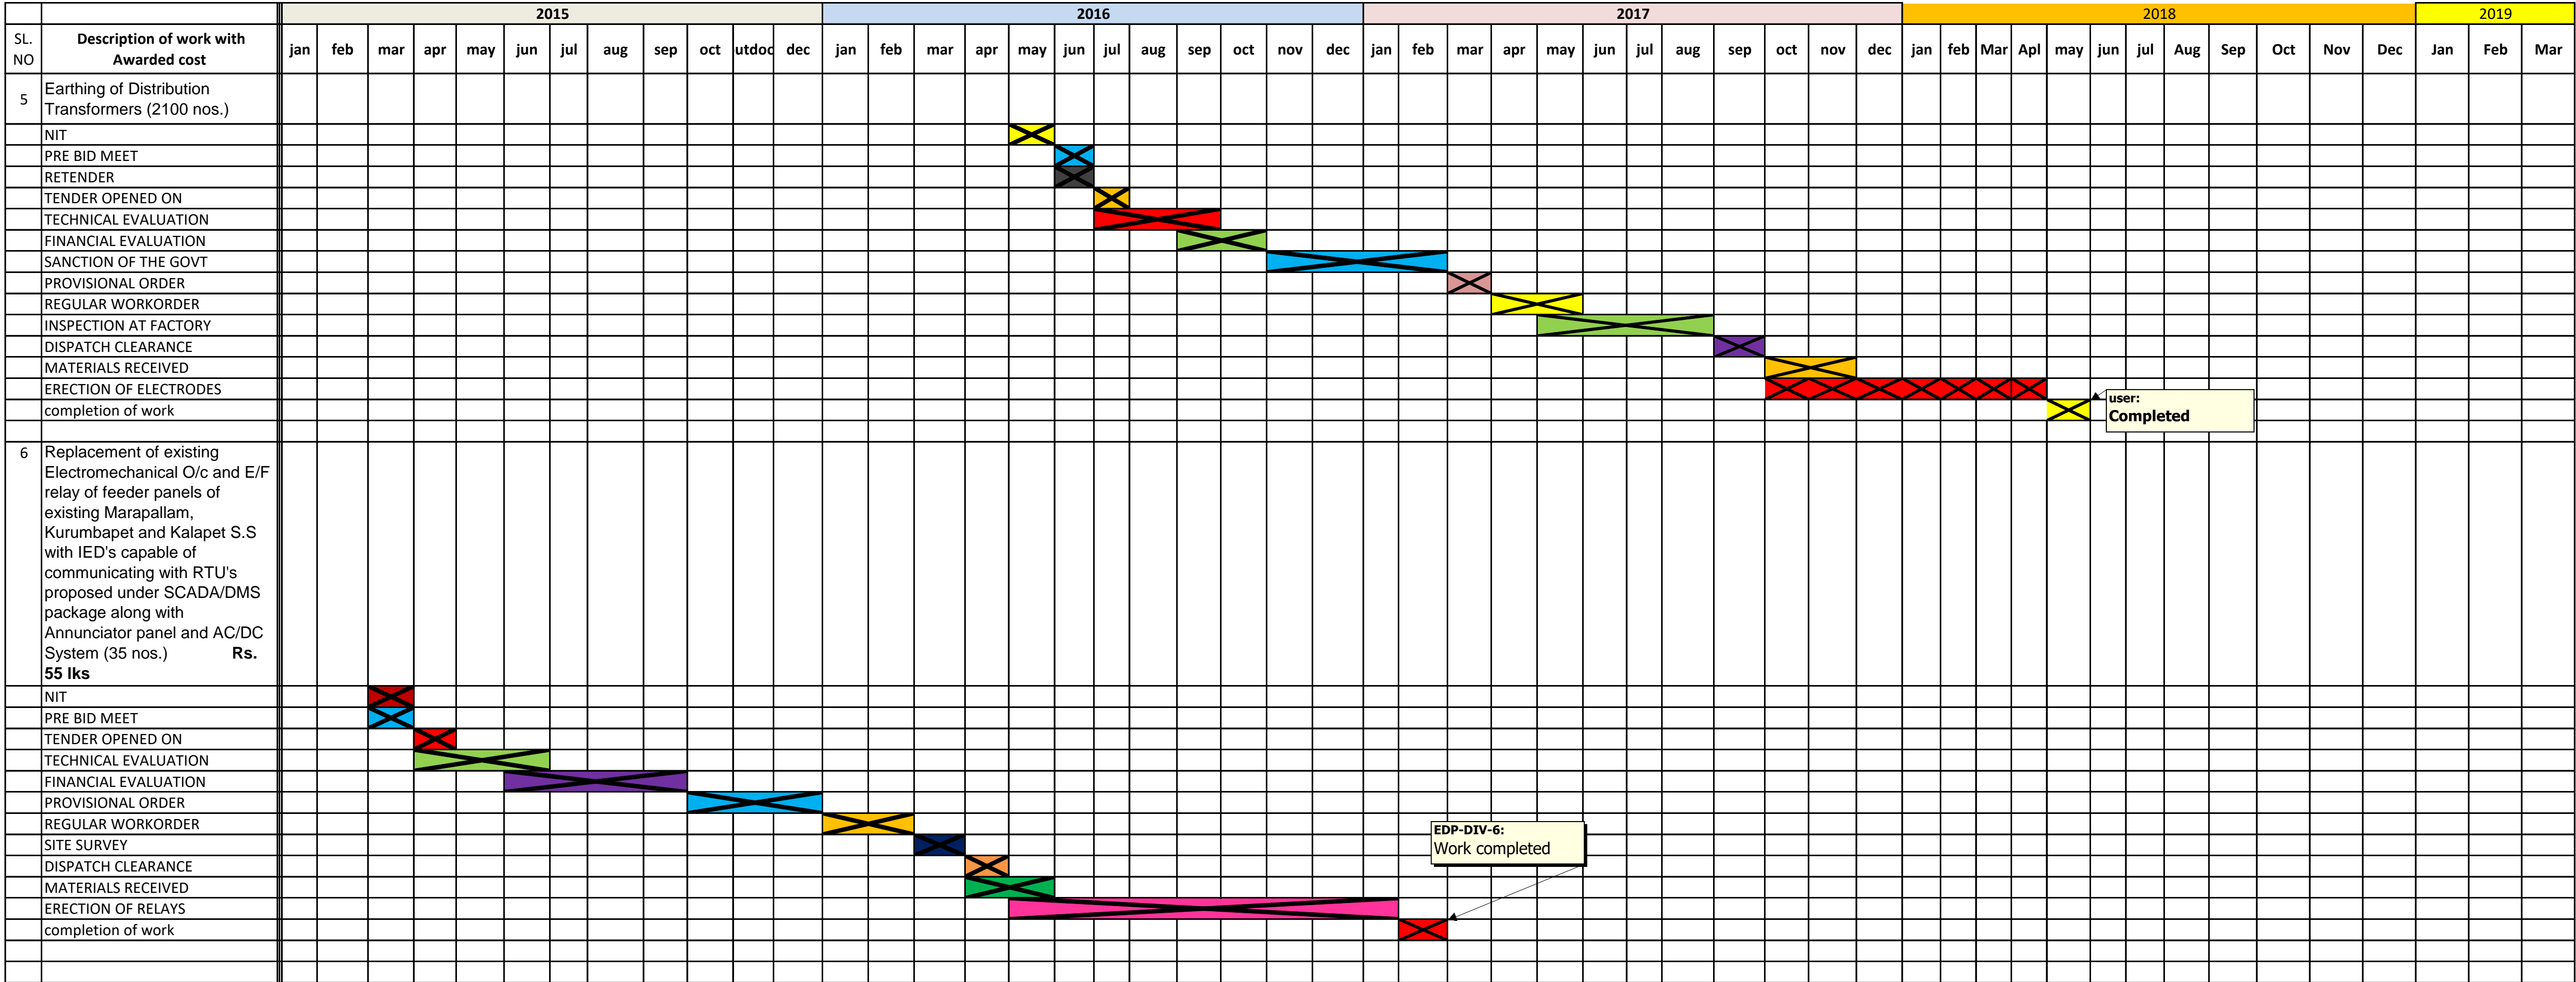

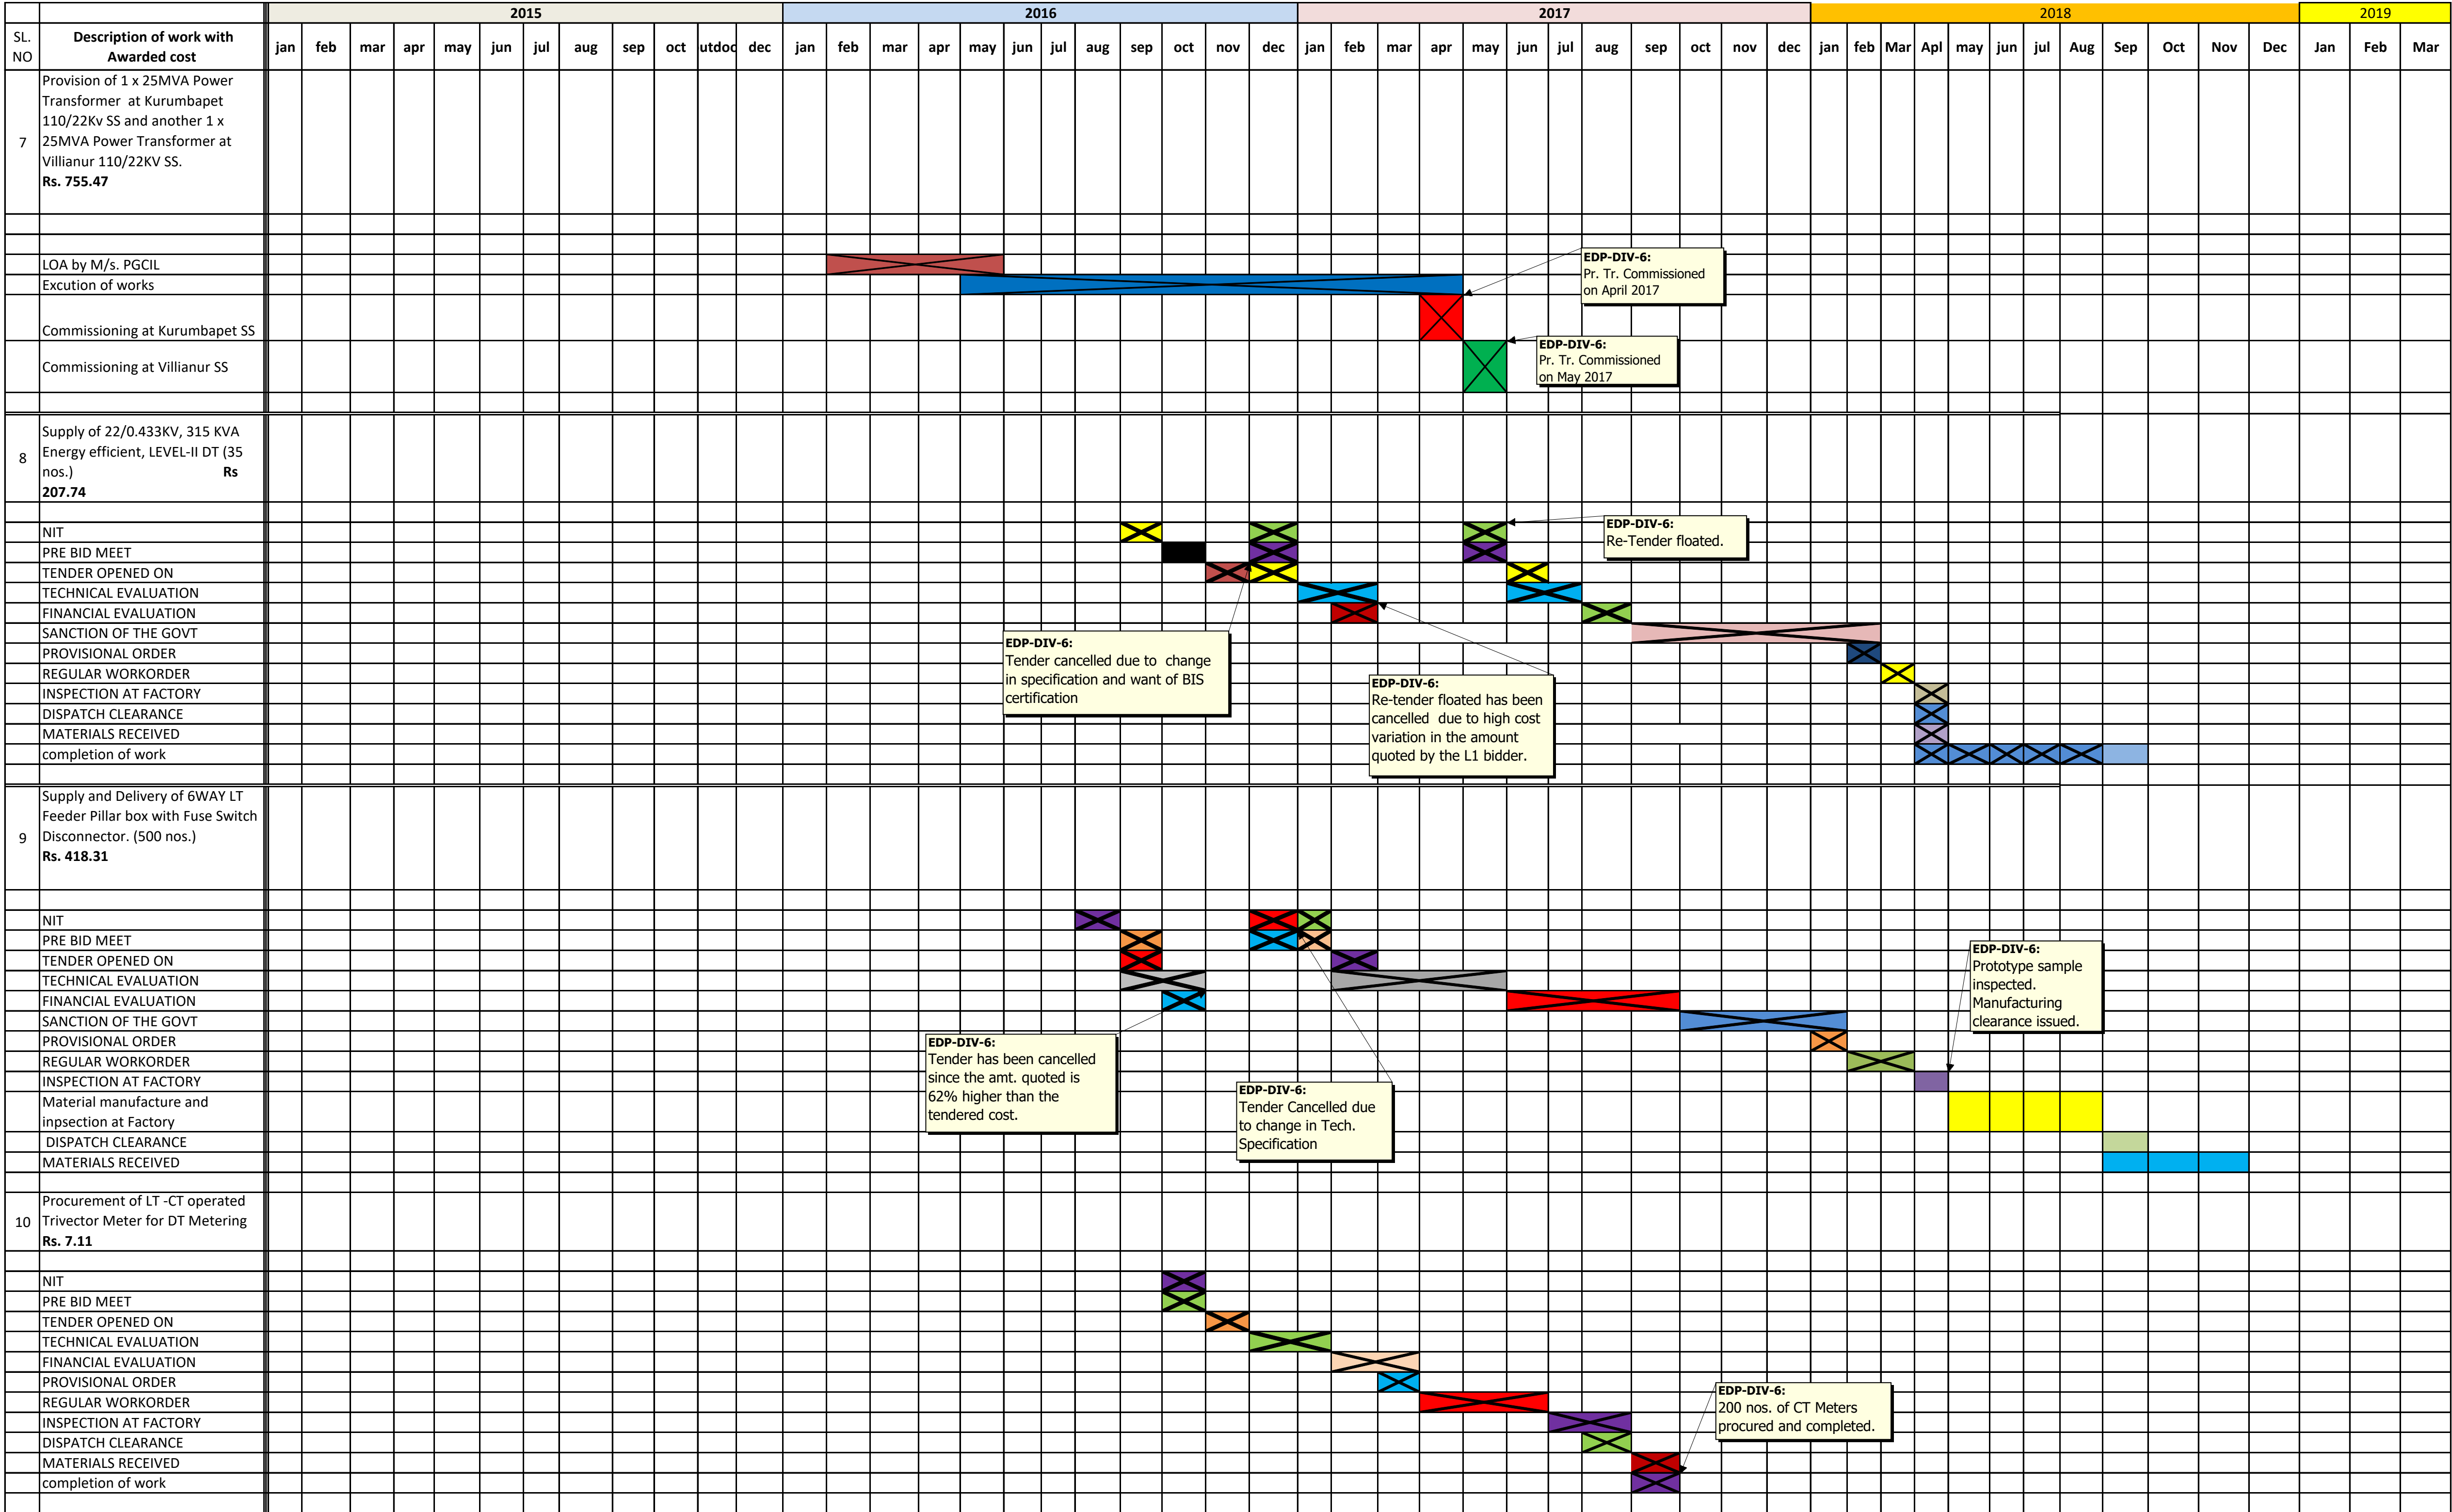

[illegible][illegible][illegible]

